


# West Fork of the San Jacinto River Emergency Dredging

**Current Status:** Dredging began 20 September 2018, both Dredges are working with no issues. As of 21 January 2019 Project is at approximately at 45% Complete.

WEST FORK SAN JACINTO RIVER EMERGENCY DEBRIS REMOVAL PROJECT

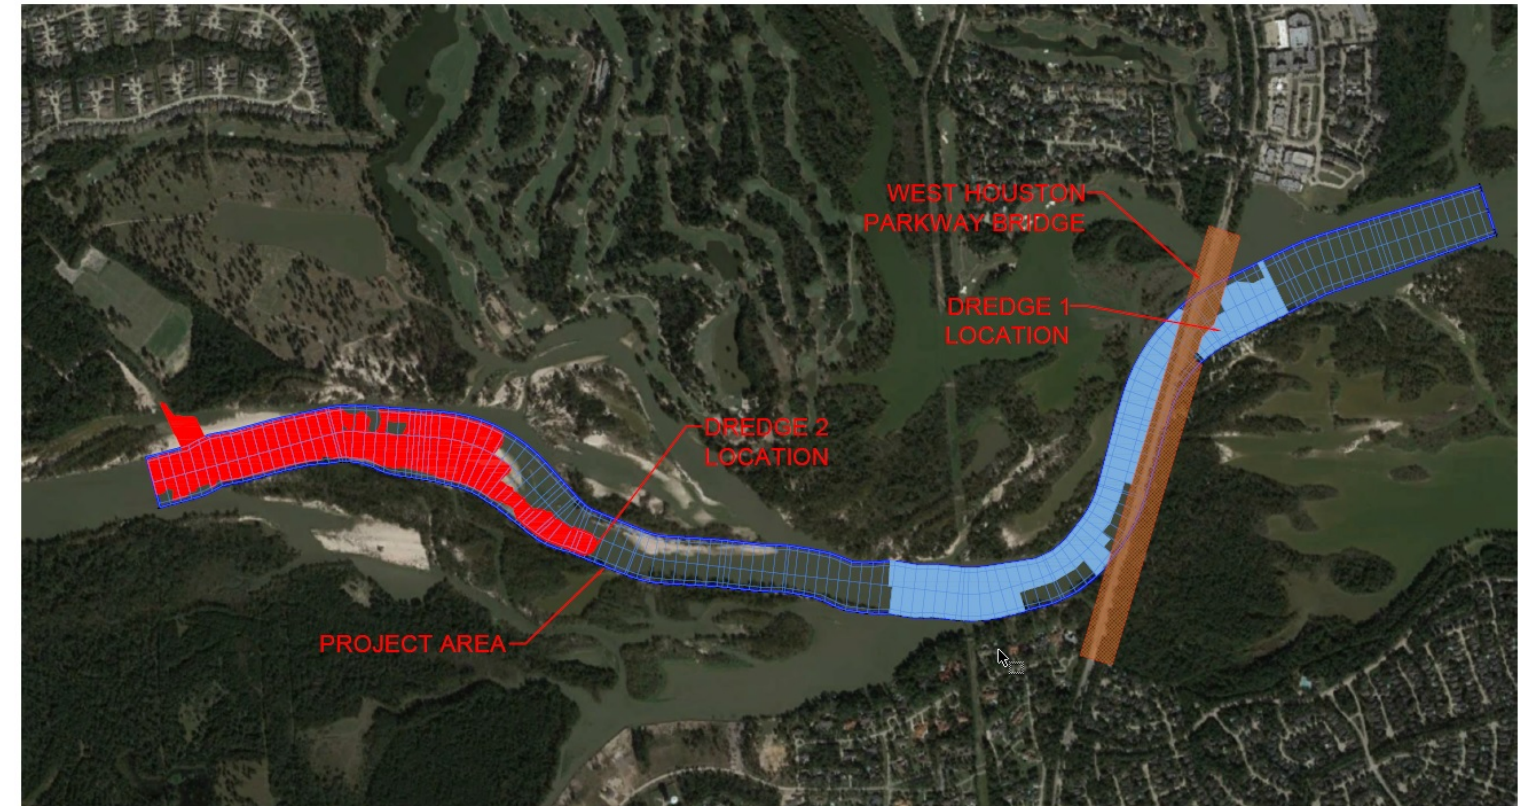

**DREDGE 2 PROGRESS**  
THROUGH FEBRUARY 4, 2019

**DREDGE 1 PROGRESS**  
THROUGH FEBRUARY 4, 2019



**Update:**

Dredge 1 – Average 3,940 cy Dig/Day over the past week with 56% run time and average travel of 110 lf/day. As of 30 Jan 2019 Dredge has dug approximately 284,500 cy.

Dredge 2 – Average 6,843 cy Dig/Day over the past week with 51% run time and average travel of 125 lf/day. As of 30 Jan 2019 Dredge has dug approximately 539,000 cy.

Noise Complaint – continue to monitor noise levels day and night. No further action required at this time.

**Two week look Ahead:**

Dredge 1 – continue dredging  
Dredge 2 – continue dredging

**Issues:** None

**Authorization:** FEMA Mission Assignment SWD-30

**Contract Milestones**

Activity/Milestones	Start	Finish	Solicitation Details
Set-up Staging Area	19Jul18 (A)	28Jul18(A)	Bid: \$69,814,060 S&A: \$400K Cont: \$3,490,703 Total: \$73,704,763
Assemble & Install Pipelines	28Jul18 (A)	6Oct18	
Set up Dredges (2)	13Aug18 (A)	16Oct18	
General Debris Removal & Disposal	21Sep18(A)	8Apr19	
Dredging	21Sep18(A)	14Apr19	
Demobilize & Cleanup	15Apr19	14May19	



**BUILDING STRONG®**
