Activity ID	Activity Name	Start	Finish
Project Phases: 2200B Initial Plan Formulation		15-Sep-04 A	21-Nov-07
100840.22000.22T00 Feas Prog & Projt Mgmt		27-Dec-05 A	03-Jul-06
FEA1760.1	Initial Work Allowance	27-Dec-05 A	27-Dec-0...
FEA1770.1	Receive Fed Funds	27-Dec-05 A	27-Dec-0...
FEA1771.1	Feas-Start Feasibility	03-Jul-06	
100840.22000.22A00 Public Involvement		15-Sep-06	15-Sep-06
FEA2411.1	Public Meeting	15-Sep-06	15-Sep-06
100840.22000.22C00 Socio/Economics		18-Sep-06	27-Feb-07
FEA1941.1	Baseline Analysis	18-Sep-06	27-Feb-07
100840.22000.22D00 Cultural Resources		18-Sep-06	18-Oct-06
FEA2320.1	Hist/Archival	18-Sep-06	18-Oct-06
100840.22000.22E00 Environmental		05-Jul-06	23-May-07
FEA2101.1	Baseline Analysis (Hammock)	05-Jul-06	14-May-07
FEA2103.1	With Project (Alternatives Analysis) (Hammock)	14-Jul-06	23-May-07
FEA2104.1	Sampling & Testing Invest. (water & sed quality)	14-Jul-06	17-Oct-06
FEA2070.1	NEPA Scoping Meeting	15-Sep-06	15-Sep-06
100840.22000.22F00 F&W Coordination		14-Jul-06	08-Jun-07
FEA2261.1	Agency Coordination	14-Jul-06	08-Jun-07
FEA2269.1	FW Coordination Act	14-Jul-06	08-Jun-07
100840.22000.22L00 HTRW Studies		18-Sep-06	28-Sep-06
FEA2270.1	HTRW Prelim Assmt	18-Sep-06	28-Sep-06
100840.22000.22P00 Eng & Design/Cost Est		11-Jul-06	12-Jul-07
FEA1820.1	Geo: Review/Evaluate/Assess Soils	11-Jul-06	12-Jul-06
FEA1830.1	Struc: Site Visit for Facilities Mods	11-Jul-06	13-Jul-06
FEA1840.1	Gen: Civil Analysis	11-Jul-06	14-Jul-06
FEA1850.1	H&H: ERDC - Review of Data/ New Data Collection	11-Jul-06	31-Jul-06
FEA1855.1	H&H: Galv Distr Coordination with all ERDC work (IP...	11-Jul-06	08-Jun-07
FEA1821.1	Geo: Re-plot Existing Data	13-Jul-06	24-Jul-06
FEA1831.1	Struc: Data Collection/Investigation of Existing Facilit...	14-Jul-06	20-Jul-06
FEA1841.1	Gen: Preliminary Alignments	17-Jul-06	26-Jul-06
FEA1832.1	Struc: Analysis/Evaluation of Existing Structures	21-Jul-06	03-Aug-06
FEA1822.1	Geo: Define Dredging for Alignment Alternatives	27-Jul-06	02-Aug-06

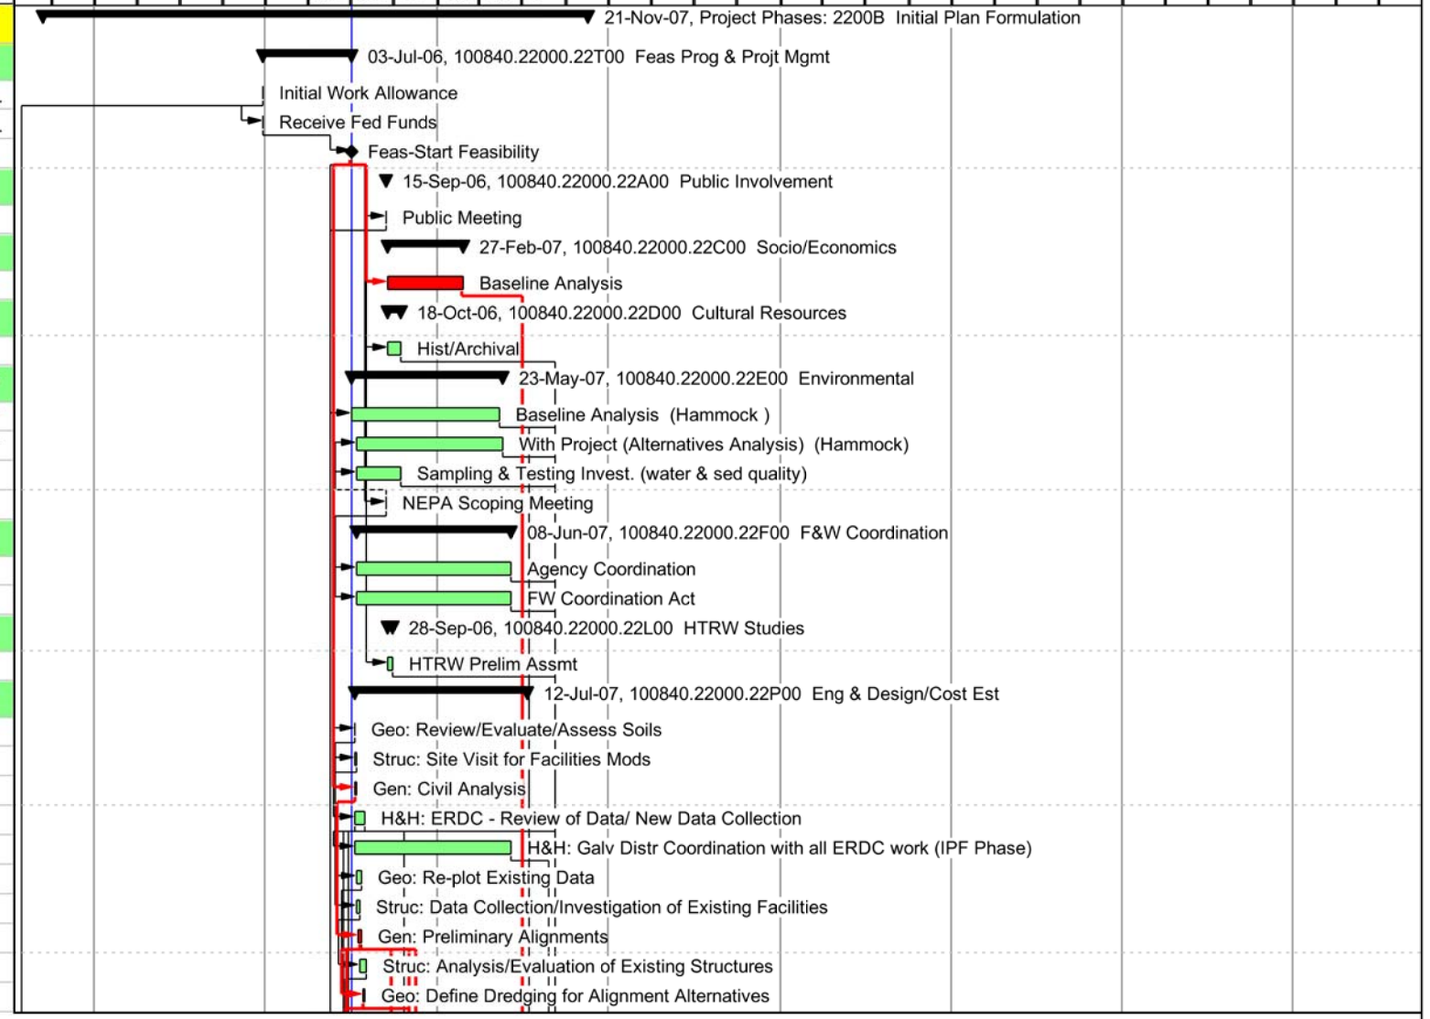

Actual Work
Remaining Work
Critical Remaining Work
Milestone
Summary

TASK filter: All Activities

© Primavera Systems, Inc.
Gilbert Gantt

Activity ID	Activity Name	Start	Finish
FEA1854.1	H&H: Review & Assess Collected data	01-Aug-06	10-Aug-06
FEA1823.1	Geo: Define Placement Areas	03-Aug-06	07-Aug-06
FEA1833.1	Struc: Quantity Takeoffs	04-Aug-06	07-Aug-06
FEA1800.1	Gen: Surveys (AE)	08-Aug-06	08-Nov-06
FEA1824.1	Geo: Identify Geotech Info Deficiencies/Summary	08-Aug-06	11-Aug-06
FEA1834.1	Struc: Review / Check	08-Aug-06	10-Aug-06
FEA1851.1	H&H: ERDC - Hydrodynamic Model 2-D	11-Aug-06	06-Dec-06
FEA1810.1	H&H: Screening (Preliminary) Evaluation	09-Nov-06	24-Nov-06
FEA1811.1	H&H: Energy Dissipator/Breakwater Evaluation	27-Nov-06	15-Dec-06
FEA1852.1	H&H: ERDC Barge Simulation	07-Dec-06	12-Jul-07
FEA1842.1	Gen: Preliminary Quantities	18-Dec-06	02-Jan-07
FEA1843.1	Gen: Relocations	03-Jan-07	10-Jan-07
FEA1844.1	Gen: Preliminary Quantities for Non-Structural Alts.	03-Jan-07	09-Jan-07
FEA1870.1	Cost: Preliminary Cost Estimates for Screening Purp...	11-Jan-07	13-Mar-07
100840.22000.22R00	**Plan Formulation**	03-Jul-06	21-Nov-07
FEA2420.1	Policy on Authorities for Screening	03-Jul-06	11-Jul-06
FEA2421.1	Identification of Applicable Problems	17-Aug-07	30-Aug-07
FEA2422.1	Formulate Without-Project Conditions	17-Aug-07	30-Aug-07
FEA2430.1	Prepare for FSM	31-Aug-07	14-Oct-07
FEA2431.1	Attend FSM	15-Oct-07	17-Oct-07
FEA2432.1	FSM Project Doc. (Documetation for FSM)	18-Oct-07	24-Oct-07
FEA2460.1	Milestone - Feasibility Scoping Meeting	25-Oct-07	25-Oct-07
FEA2440.1	Tech Review	26-Oct-07	21-Nov-07
100840.22000.22S00	**Feasibility Report**	15-Sep-04 A	03-Apr-07
FEA1010.1	Initial Plan Formulation In-House Labor	15-Sep-04 A	03-Apr-07
FEA1010.11	Intial Plan Formulation (PM) In-House Labor	03-Jul-06*	29-Sep-06
FEA1010.12	Intial Plan Formulation (PL) In-House Labor	03-Jul-06*	29-Sep-06
FEA1010.13	Intial Plan Formulation (ENG) In-House Labor	03-Jul-06*	29-Sep-06
Project Phases: 2200C	**Plan Formulation**	07-Dec-06	22-Jul-09
100840.22000.22C00	**Socio/Economics**	26-Oct-07	07-Mar-08
FEA1990.2	NED Benefit Analysis	26-Oct-07	10-Dec-07
FEA1940.2	Traffic Data Analysis	26-Oct-07	24-Jan-08
FEA1941.2	Transportation Cpst Analyses/Casualty Analysis (Co...	26-Oct-07	07-Mar-08
100840.22000.22D00	**Cultural Resources**	26-Oct-07	22-Jul-09
FEA2331.2	Data Recovery (Contracts)	26-Oct-07	17-Sep-08
FEA2321.2	National Register Eligibilty	18-Sep-08	16-Mar-09
FEA2341.2	SHPO Concurrence	17-Mar-09	22-Jul-09
100840.22000.22E00	**Environmental**	26-Oct-07	10-Mar-08

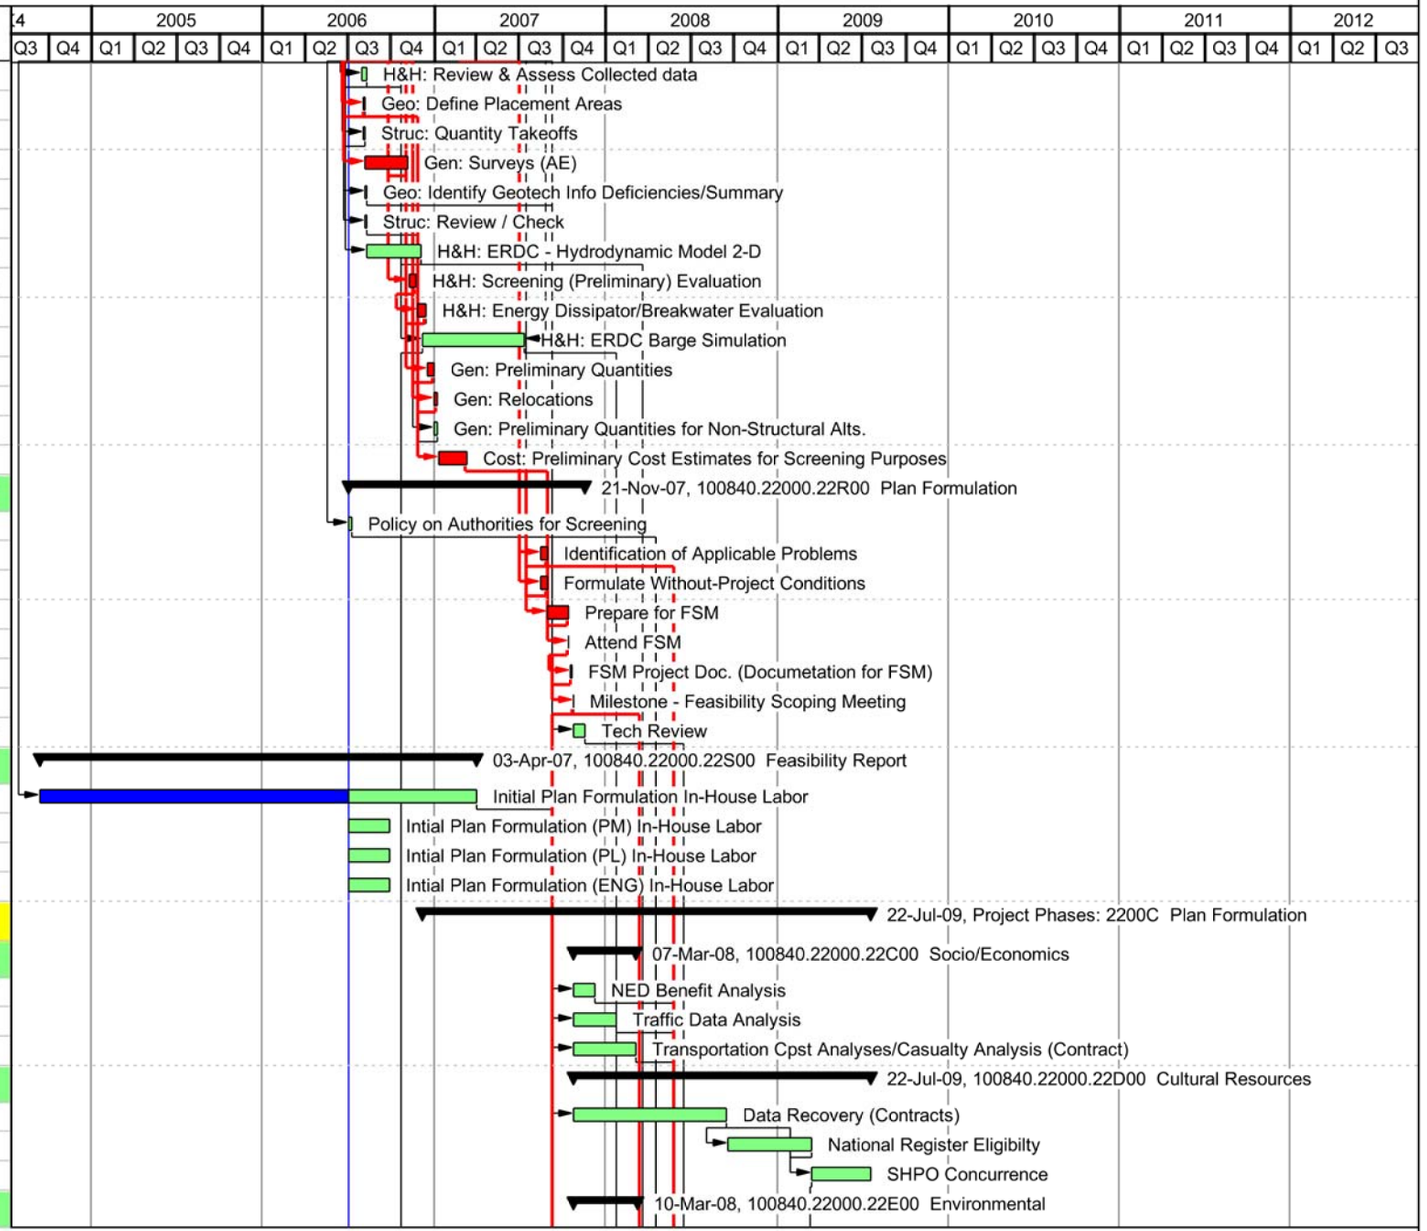

© Primavera Systems, Inc.
Gilbert Gantt

Activity ID	Activity Name	Start	Finish
FEA2103.2	With Project (Alternatives Analysis) (Hammock)	26-Oct-07	10-Mar-08
FEA2160.2	Sec 404(b)(1) Analysis	26-Oct-07	31-Dec-07
FEA2163.2	Mitigation Plan Development (Hammock)	26-Oct-07	10-Mar-08
FEA2165.2	Impact Analysis (Hammock)	26-Oct-07	10-Mar-08
100840.22000.22F00	**F&W Coordination**	26-Oct-07	18-Apr-08
FEA2269.2	USFWS Coordination Act Report	26-Oct-07	18-Apr-08
FEA2261.2	Resource Agency Coordination (Hammock)	26-Oct-07	18-Apr-08
FEA2263.2	Section 7 Consultation	26-Oct-07	24-Jan-08
FEA2265.2	Essential Fish Habitat Evaluation	26-Oct-07	24-Jan-08
100840.22000.22H00	**Real Estate**	26-Oct-07	12-Dec-07
FEA2010.2	Preparation of Gross Appraisal	26-Oct-07	08-Nov-07
FEA2060.2	Evaluation of Alternative Plans	26-Oct-07	01-Nov-07
FEA2062.2	Preparation of Baseline Cost Estimate	02-Nov-07	05-Nov-07
FEA2063.2	Surveying and Mapping	06-Nov-07	20-Nov-07
FEA2040.2	Preparation of Legal Opinion/ Compensability	09-Nov-07	16-Nov-07
FEA2064.2	Ownership Data Compilation	21-Nov-07	28-Nov-07
FEA2065.2	GIS Data Entry and Maintenance	29-Nov-07	12-Dec-07
100840.22000.22L00	**HTRW Studies**	26-Oct-07	29-Oct-07
FEA2270.2	HTRW Analysis	26-Oct-07	29-Oct-07
100840.22000.22P00	**Eng & Design/Cost Est**	07-Dec-06	07-Sep-08
FEA1815.2	Gen: ERDC-CHL Coordination	07-Dec-06	12-Dec-06
FEA1820.2	Geo: Develop Task Order SOW for Core Drilling and...	26-Oct-07	16-Nov-07
FEA1851.2	H&H: ERDC - Sediment Study	26-Oct-07	02-Jan-08
FEA1822.2	H&H: Galv District Coordination with all ERDC work (...	26-Oct-07	13-Jun-08
FEA1821.2	Geo: Core Drilling & Testing Contract	19-Nov-07	22-Feb-08
FEA1813.2	H&H: Environmental Coordination	02-Jan-08	08-Jan-08
FEA1812.2	Struc: Analysis & Design Review	25-Feb-08	07-Mar-08
FEA1830.2	Struc: Quantity Takeoffs	10-Mar-08	26-Mar-08
FEA1840.2	Gen: Civil Analysis - Navigation Channel	11-Mar-08	07-Apr-08
		14-Apr-08	17-Apr-08
FEA1824.2	Geo: New Work Dredge Material Placement Plan	16-Apr-08	25-Apr-08
FEA1845.2	Gen: Civil Analysis - Breakwater	18-Apr-08	22-Apr-08
FEA1846.2	Gen: Civil Quantities	23-Apr-08	01-May-08
FEA1825.2	Geo: Maintenance Work Dredge Material Placement ...	28-Apr-08	07-May-08
FEA1847.2	Gen: Non-Structural Alts. Quantities	02-May-08	05-May-08

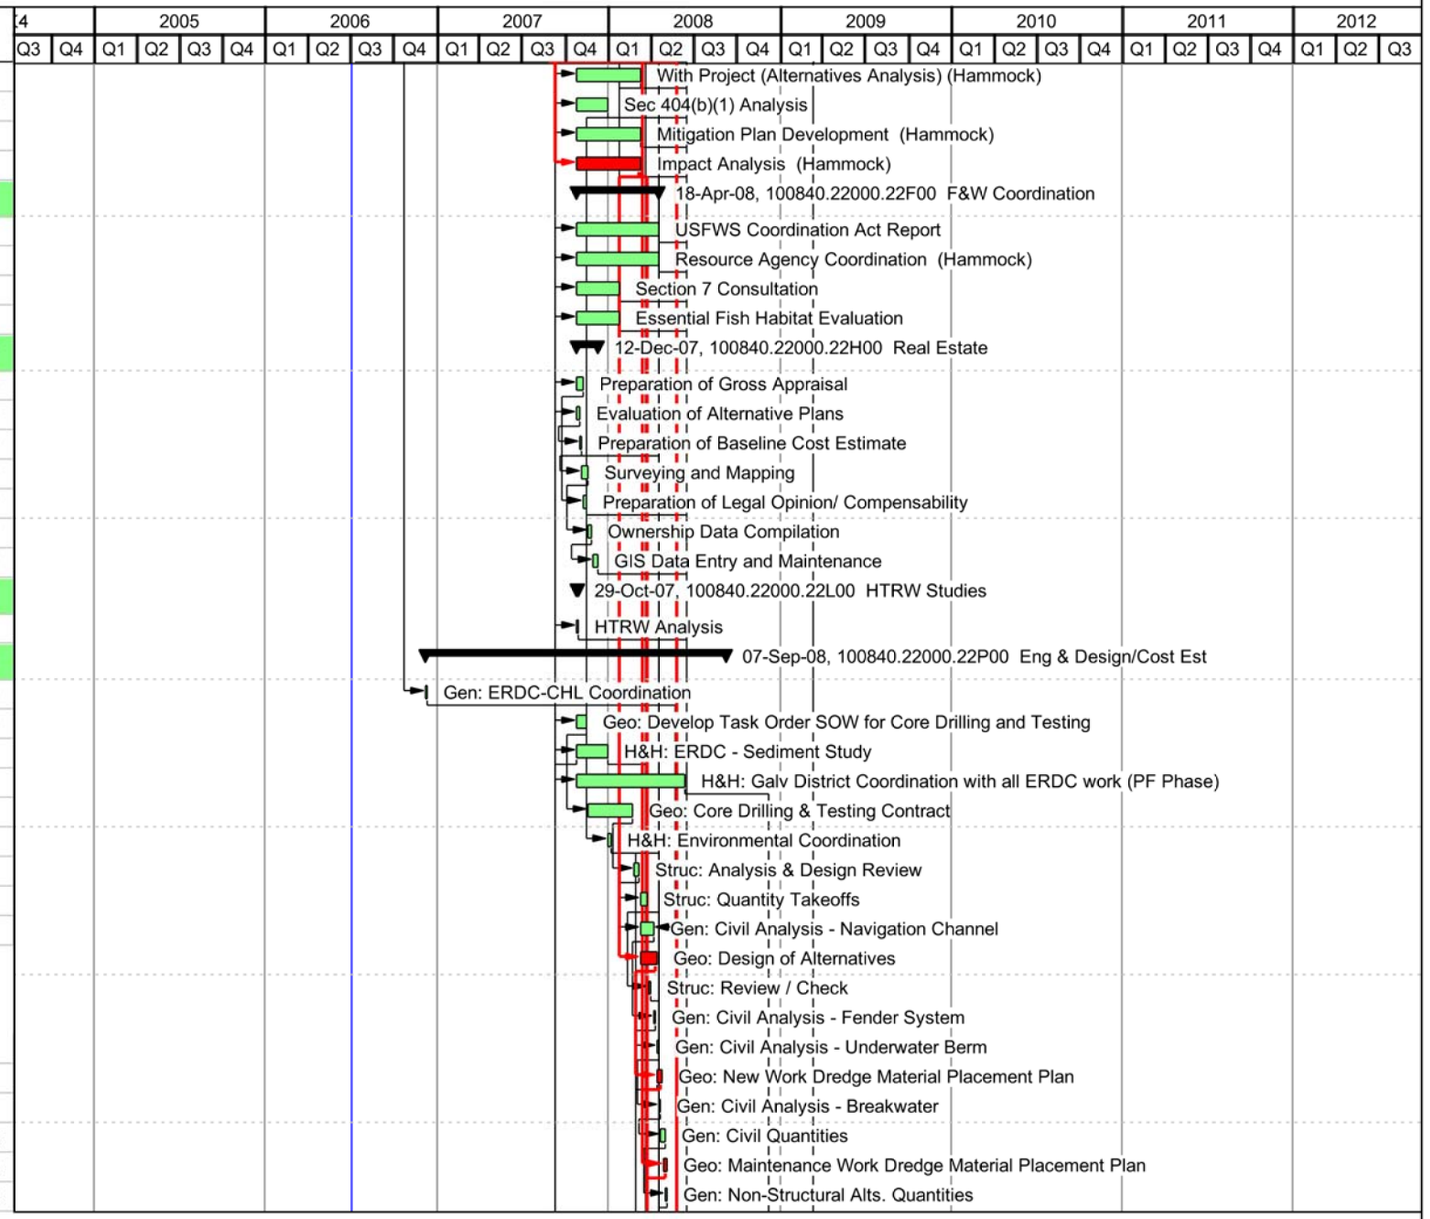

© Primavera Systems, Inc.
Gilbert Gantt

Activity ID	Activity Name	Start	Finish
FEA1826.2	Geo: Preliminary Design of Upland Sites	08-May-08	14-May-08
FEA1827.2	Geo: Preliminary BUDM Design	15-May-08	21-May-08
FEA1828.2	Geo: Preliminary Erosion Protection Design	22-May-08	30-May-08
FEA1829.2	Geo: Review and Approval	02-Jun-08	03-Jun-08
FEA1870.2	Cost: Cost Estimates for Refined Screening Purposes	04-Jun-08	09-Jul-08
FEA1872.2	VE Study	10-Jul-08	07-Sep-08
100840.22000.22R00	**Plan Formulation**	04-Jun-08	11-Sep-08
FEA2420.2	Long-Term Disposal Base Plan Selection	04-Jun-08	17-Jun-08
FEA2421.2	Alternative Plans for Navigation Problems	10-Jul-08	30-Jul-08
FEA2422.2	Optimization of Naviation Problems	10-Jul-08	23-Jul-08
FEA2460.2	Milestone - Identify Selected Plan	31-Jul-08	31-Jul-08
FEA2440.2	Tech Review	01-Aug-08	11-Sep-08
100840.22000.22S00	**Feasibility Report**	26-Oct-07	18-Jul-08
FEA1010.2	Plan Formulation In-House Labor	26-Oct-07	18-Jul-08
Project Phases: 2200D	**Final Plan Formulation**	16-Apr-08	05-Jan-10
100840.22000.22A00	**Public Involvement**	01-Aug-08	19-Sep-08
FEA2375.3	Public Meeting	01-Aug-08	19-Sep-08
100840.22000.22C00	**Socio/Economics**	01-Aug-08	05-May-09
FEA1940.3	Traffic Data Analysis	01-Aug-08	27-Oct-08
FEA1941.3	Transportation Cpst Analyses/Casualty Analysis (Co...	28-Oct-08	10-Mar-09
FEA1990.3	NED Benefit Analysis	11-Mar-09	21-Apr-09
FEA2425.3	Detailed Economic Evaluation	22-Apr-09	05-May-09
100840.22000.22D00	**Cultural Resources**	28-Apr-09	29-Jul-09
FEA2320.3	Cult Res Impact Eval & Final SHPO Coord	28-Apr-09	29-Jul-09
100840.22000.22E00	**Environmental**	01-Aug-08	23-Dec-08
FEA2103.3	With Project (Alternatives Analysis) (Hammock)	01-Aug-08	23-Dec-08
FEA2160.3	Sec 404(b)(1) Analysis	01-Aug-08	02-Sep-08
	Socioeconomic Profile & Impact Asmt Costs (Hamm...	01-Aug-08	27-Oct-08
100840.22000.22F00	**F&W Coordination**	01-Aug-08	27-Oct-08
FEA2261.3	Resource Agency Coordination (Hammock)	01-Aug-08	27-Oct-08
FEA2263.3	Section 7 Consultation	01-Aug-08	27-Oct-08
FEA2265.3	Essential Fish Habitat Evaluation	01-Aug-08	27-Oct-08
100840.22000.22H00	**Real Estate**	01-Aug-08	11-Sep-08
FEA2000.3	Preparation of REP	01-Aug-08	14-Aug-08

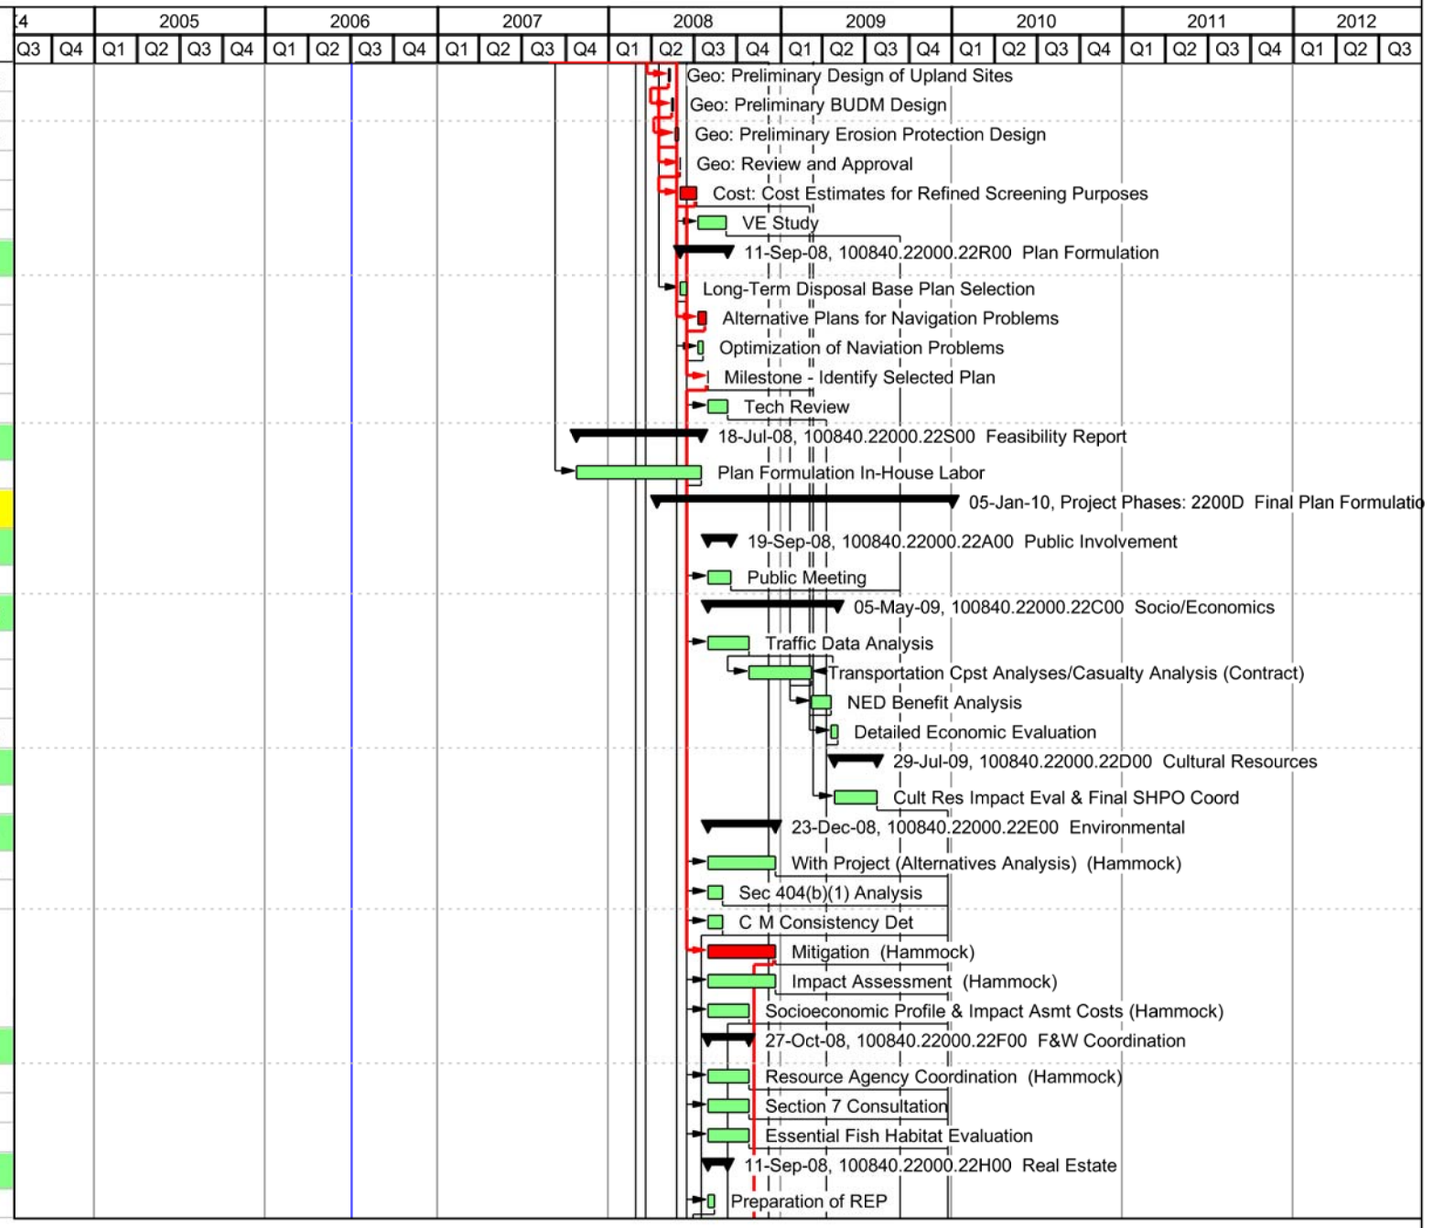

© Primavera Systems, Inc.
Gilbert Gantt

Activity ID	Activity Name	Start	Finish
FEA2060.3	Preparation of PCA	15-Aug-08	28-Aug-08
FEA2061.3	Relocations of Facilities/Utilities	29-Aug-08	02-Sep-08
FEA2062.3	Internal Review	03-Sep-08	04-Sep-08
FEA2063.3	Comment Response	05-Sep-08	11-Sep-08
100840.22000.22L00	**HTRW Studies**	01-Aug-08	04-Aug-08
FEA2270.3	HTRW Analysis	01-Aug-08	04-Aug-08
100840.22000.22P00	**Eng & Design/Cost Est**	16-Apr-08	30-Mar-09
FEA1810.3	H&H: Placement Area Assistance/Coordination	16-Apr-08	06-May-08
FEA1811.3	H&H: Report Write-Up and Reviews	07-May-08	23-Oct-08
FEA1820.3	Geo: Finalize Placement Plans	01-Aug-08	06-Aug-08
FEA1830.3	Struc: Placement Area Investigation and Data Collec...	01-Aug-08	05-Aug-08
FEA1844.3	Gen: Draft Engineering Appendix - Civil Analysis	01-Aug-08	11-Aug-08
FEA1832.3	Struc: Analysis of Placement Area Structures	06-Aug-08	15-Aug-08
FEA1821.3	Geo: Finalize Upland Site Design	07-Aug-08	12-Aug-08
		19-Aug-08	07-Oct-08
FEA1843.3	Gen: Draft Engineering Appendix - Civil Write-Up	19-Aug-08	27-Aug-08
FEA1823.3	Geo: Final Shore Protection Design	21-Aug-08	26-Aug-08
FEA1824.3	Geo: Final DMMP	27-Aug-08	02-Sep-08
FEA1834.3	Struc: Preliminary Draft Write-Up	02-Sep-08	08-Sep-08
FEA1825.3	Geo: Draft Write-Up for Engineering Appendix	03-Sep-08	16-Sep-08
FEA1835.3	Struc: Review and Finalize Draft Write-Up (Structural)	09-Sep-08	15-Sep-08
FEA1836.3	Struc: CADD Drawings	16-Sep-08	02-Oct-08
FEA1826.3	Geo: Plates, Figures, and Exhibits	17-Sep-08	02-Oct-08
FEA1827.3	Geo: Review and Final Draft Write-Up (Geotech)	03-Oct-08	14-Oct-08
FEA1837.3	Struc: Review / Check CADD	03-Oct-08	03-Oct-08
FEA1870.3	Cost: Cost Estimates for Selected Plan	24-Dec-08	23-Mar-09
FEA1860.3	Compile Engineering Appendices	24-Mar-09	30-Mar-09
100840.22000.22R00	**Plan Formulation**	10-Jul-08	29-Oct-09
FEA2424.3	Long-Term Disposal Plan Selection	10-Jul-08	16-Jul-08
FEA2420.3	Plan Formulation	01-Aug-08	08-Aug-08
FEA2422.3	Alternative Plans for Long-Term Disposal	01-Aug-08	11-Aug-08
FEA2426.3	Cost Allocation and Apportionment	01-Aug-08	14-Aug-08
FEA2428.3	Conduct Planning ITR	01-Aug-08	26-Sep-08
FEA2423.3	Optimization of Plans for Long-Term Disposal	12-Aug-08	25-Aug-08
FEA2421.3	Navigation Plan Selected	24-Mar-09	30-Mar-09
FEA2427.3	Conduct Appendice ENC ITR / Incorporate comments	31-Mar-09	26-May-09

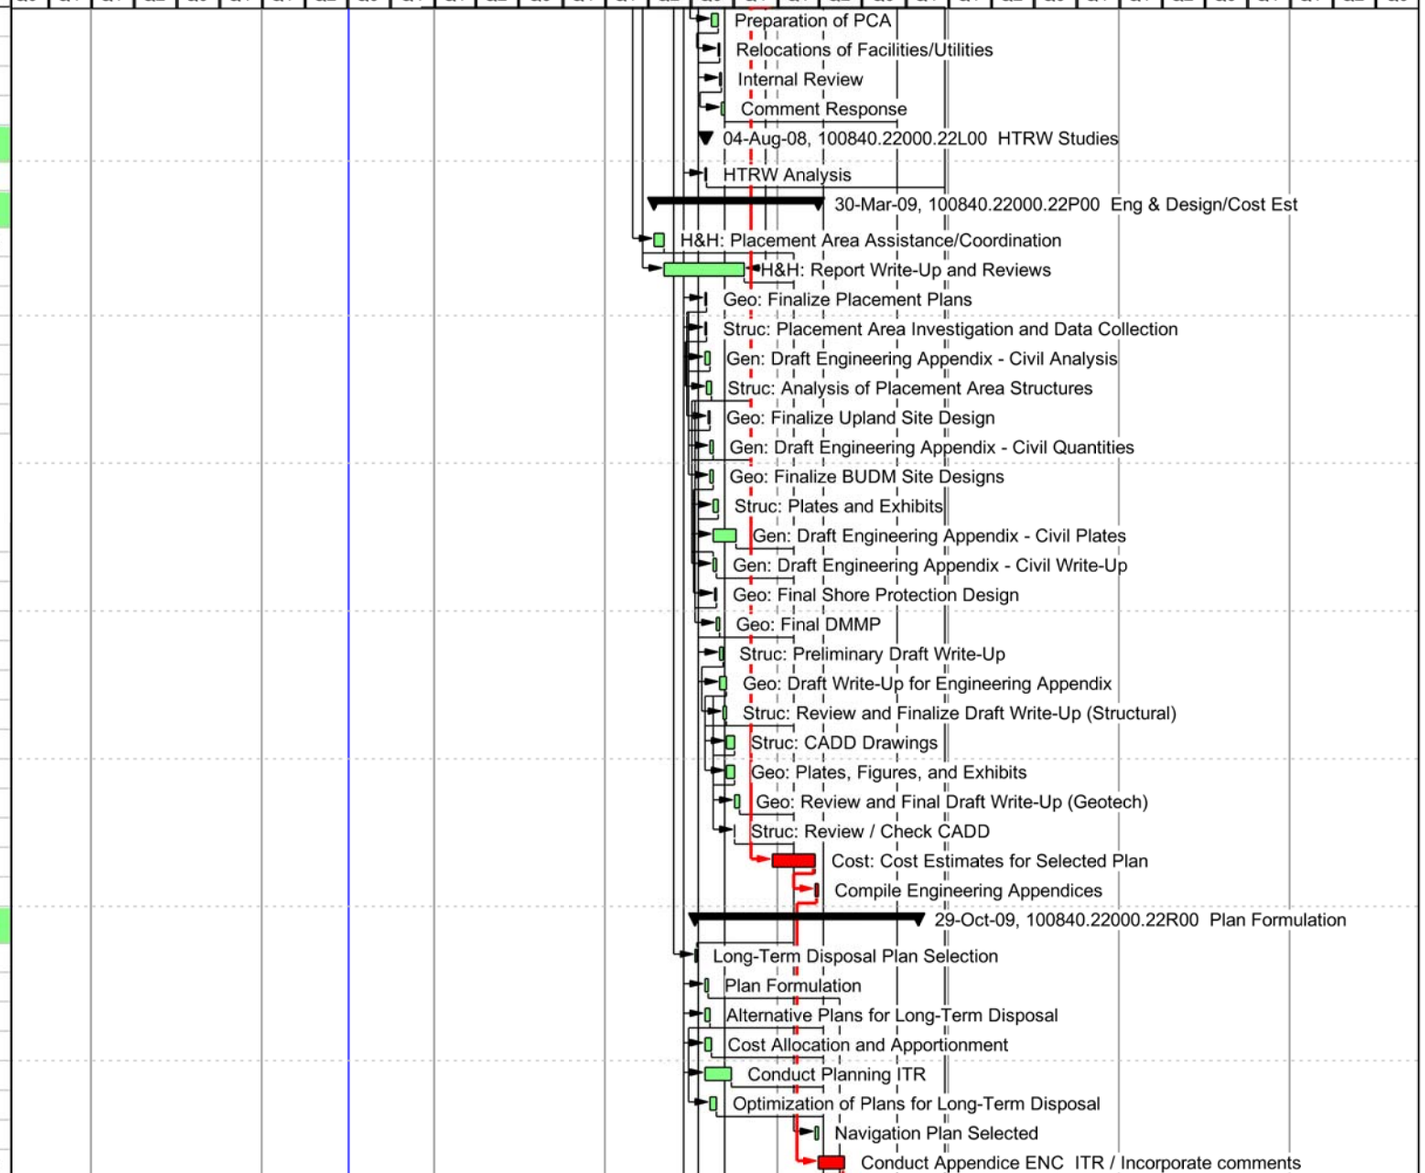

© Primavera Systems, Inc.
Gilbert Gantt

Activity ID	Activity Name	Start	Finish
FEA2440.3	Tech Review	27-May-09	29-Jun-09
FEA2455.3	Prepare for AFB	30-Jun-09	01-Sep-09
FEA2451.3	Alternative Formulation Briefing (AFB)	02-Sep-09	28-Oct-09
FEA2460.3	Milestone - AFB	29-Oct-09	29-Oct-09
100840.22000.22S00	**Feasibility Report**	01-Aug-08	05-Jan-10
FEA1010.3	Final Plan Formulation In-House Labor	01-Aug-08	09-Nov-09
FEA2463.3	Draft Feasibility Report Prep	29-Oct-09	05-Jan-10
Project Phases: 2200E	**Report Prep & Approval**	03-Sep-08	24-Sep-10
100840.22000.22E00	**Environmental**	03-Sep-08	15-Jun-10
FEA2240.4	C M Consistency Det	03-Sep-08	28-Nov-08
FEA2160.4	Sec 404(b)(1) Analysis	30-Oct-09	05-Nov-09
FEA2170.4	Water Quality Cert	06-Nov-09	04-Feb-10
FEA2180.4	Feas Water Quality Certification	05-Feb-10	05-Feb-10
FEA2100.4	DEA	08-Feb-10	15-Jun-10
100840.22000.22S00	**Feasibility Report**	28-Oct-08	24-Sep-10
FEA2200.4	Feas FONSI signed	28-Oct-08	28-Oct-08
FEA2481.4	Incorporate Comments/Print Draft Report	29-Oct-09	27-Nov-09
FEA1010.4	Final Feasibility Phase In-House Labor	10-Nov-09	30-Apr-10
FEA2213.4	Draft Report Coordination	06-Jan-10	19-Mar-10
FEA2610.4	Final Feas Report/NEPA	22-Mar-10	22-Jun-10
FEA2630.4	Submit Final Feas Report	23-Jun-10	23-Jun-10
FEA2612.4	Washington Review Cycle	24-Jun-10	24-Sep-10
No Project Phases		01-Jul-04 A	28-Sep-07
100840.1	**FY07 Budget (FED / Non-FED)**	02-Oct-06	28-Sep-07
FY0701	Programs & Project Management	02-Oct-06	28-Sep-07
FY0702	Planning, Environmental & Reg Division	02-Oct-06	28-Sep-07
FY0703	Engineering & Construction Division	02-Oct-06	28-Sep-07
FY0704	District Branches	02-Oct-06	28-Sep-07
FY0706	Real Estate	02-Oct-06	28-Sep-07
FY0705	Operations Division	02-Oct-06	28-Sep-07
FY0707	OTHER: WKBOTHCOE & Non-Labor	02-Oct-06	28-Sep-07
100840.21000.21T00	**Recon Prog & Proj Mgmt**	03-Jul-06	03-Jul-06
REC1050	Start Recon	03-Jul-06	
100840.21000.21R00	**Plan Formulation & Eval.**	01-Jul-04 A	05-Apr-07
REC1451	Reconnaissance In-House Labor	01-Jul-04 A	05-Apr-07
100840.21000.21S00	**Recon Report/Sec 905(b)**	03-Jul-06	16-Aug-06
REC1510	Submit Draft Recon Rpt		03-Jul-06

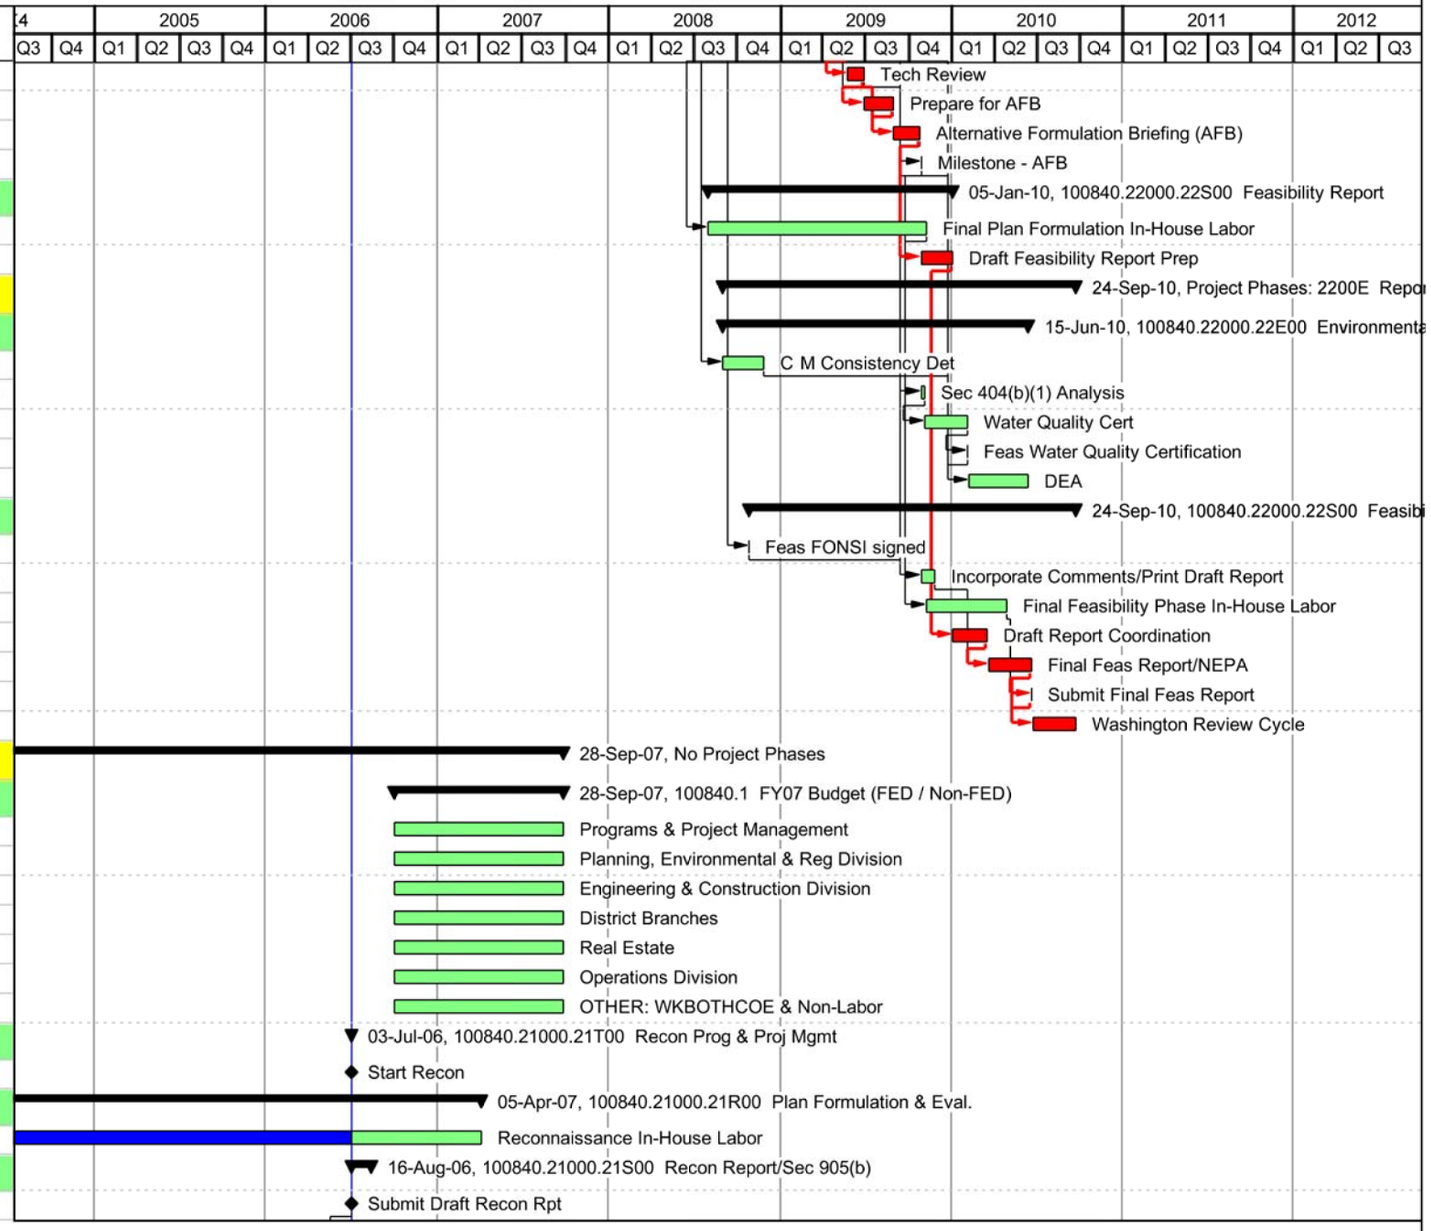

© Primavera Systems, Inc.
Gilbert Gantt

Activity ID	Activity Name	Start	Finish
REC1520	MSC/HQ Review	03-Jul-06	01-Aug-06
REC1550	HQ Policy Review	03-Jul-06	25-Jul-06
REC1560	HQ Guid/Apprv Memo	25-Jul-06	15-Aug-06
REC1570	Recon Review Conference		15-Aug-06
REC1610	Recon Guidance Memo Complete		15-Aug-06
REC1620	Recon Report Approval	15-Aug-06	16-Aug-06
5..4A.cb5...cb5)..II1eSD		15-Aug-06	02-Nov-06
REC1640	Start FCSA Development	15-Aug-06	
REC1670	Draft FCSA	15-Aug-06	22-Aug-06
REC1680	Submit FCSA		22-Aug-06
REC1690	MSC/HQ Review	22-Aug-06	27-Sep-06
REC1700	HQ Guid/Apprv Memo	27-Sep-06	02-Nov-06
REC1710	FCSA Approved		02-Nov-06
REC1720	Signed/Executed FCSA		02-Nov-06
REC1730	All Other FCSA Docs	02-Nov-06	02-Nov-06

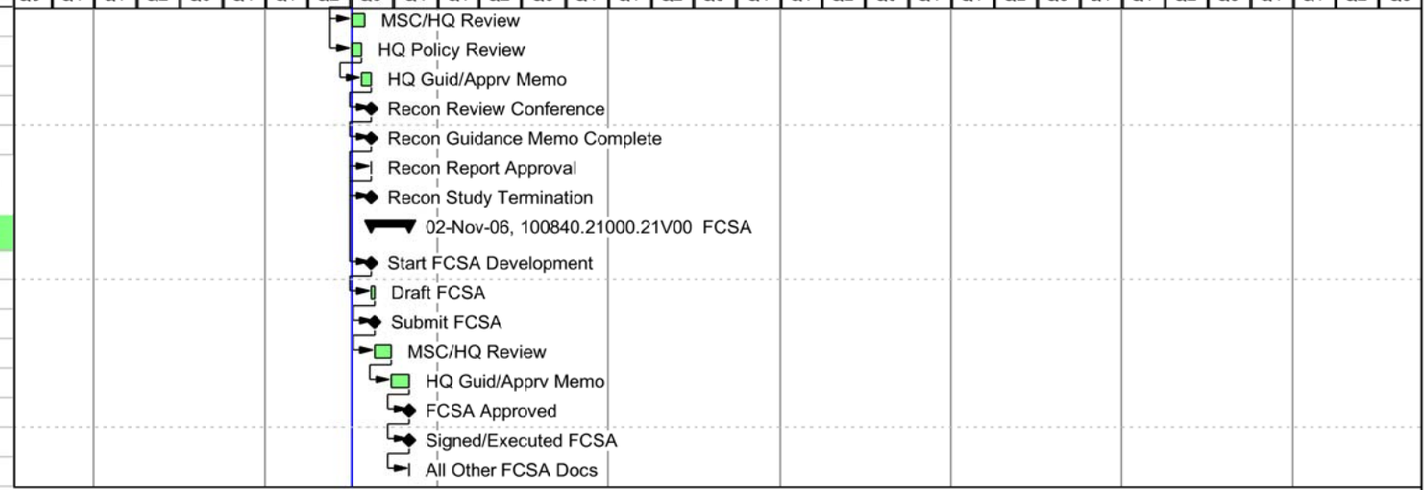

© Primavera Systems, Inc.
Gilbert Gantt
